

Addison Township Public Library


New Building Update

Date: 8/18/2026



Construction Progress and Updates

- Front pillars with engraved bricks have been completed. (some minor cracking in mortar has been observed, repairs will be made)
- All plans for Mechanical, Electrical and Plumbing have been completed and provided to the Township. Have approval to proceed.
- HVAC equipment has been ordered. Contractor is asking for a down payment, expect invoice. Planning for HVAC equipment to arrive next week.
- Final site grading will follow immediately after the rear patio is installed.
- Egress window installation in progress, 3 of 4 have been installed.
 - o Underground conduit for parking lot lighting was interfering with north east egress window. Conduit was re-routed to accommodate egress window installation. (~\$2k)
- Low-voltage (communication wiring) can be installed at this time. TLN will be consulted and help with coordinating installation.

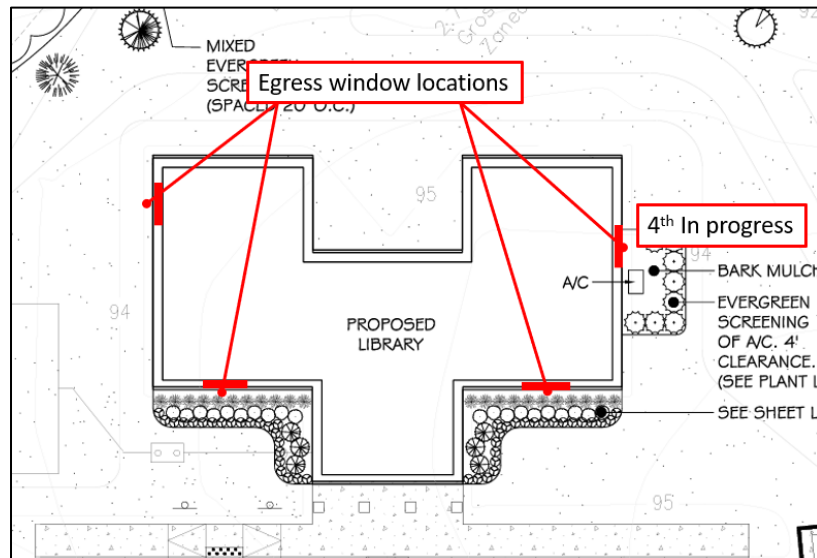

Committee Tasks

- Continuing communication with TLN to coordinate building electrical and data wiring.
 - o Requirements for IT equipment in basement has been provided to southeast commercial. Installation is being planned.
- Work with South East Commercial on interior finishes
- Review potential options for exterior signage on the building (“Addison Township Public Library” sign) shown below.
 - o Committee should start talking to Southeast to understand sign lighting and any special sign requirements.
 - o Concepts shown below

Sign Company Rendering



Architect Rendering





Progress Pictures

Pillars with engraved bricks



Egress Windows

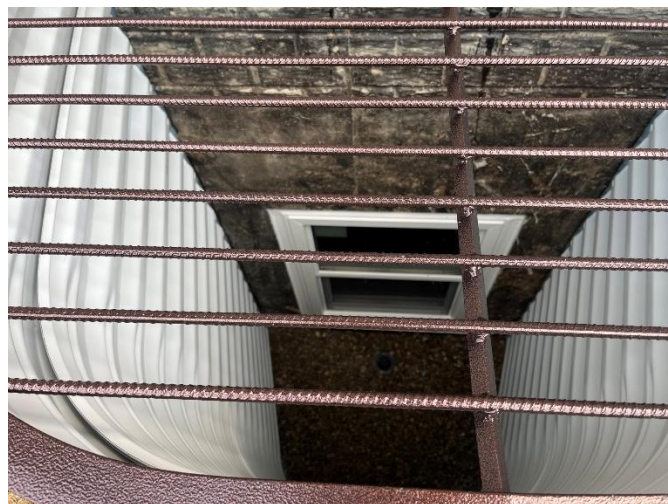

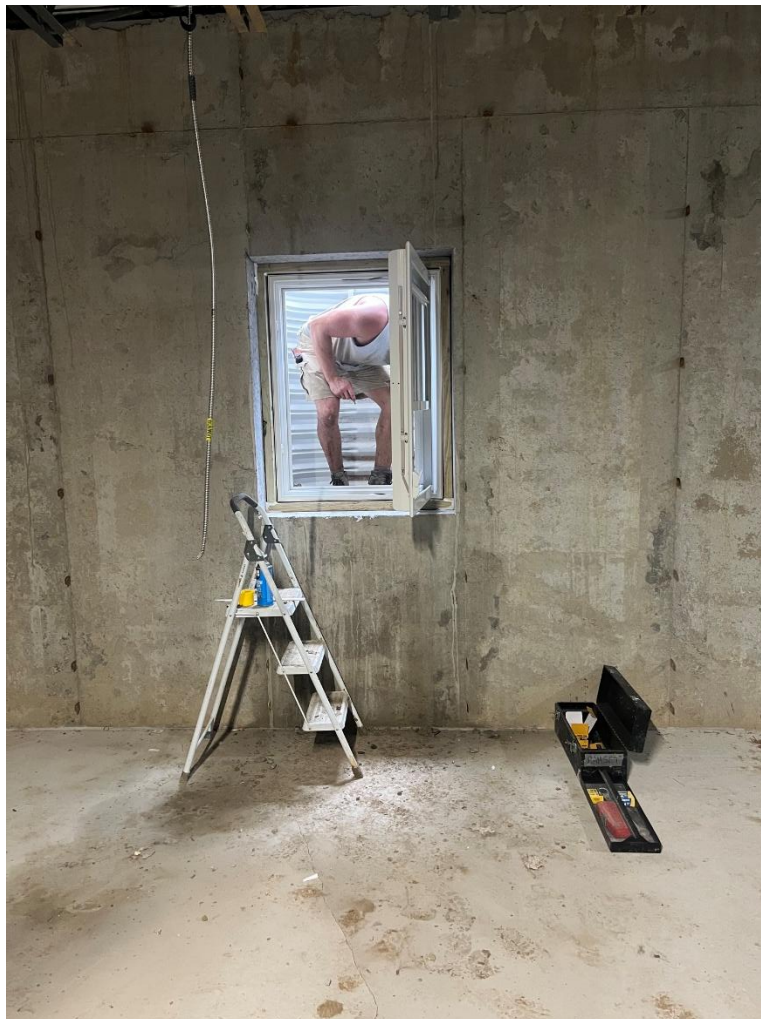

Underground Conduit Routed In Egress Window Area



(Rerouted)



Reclaimed Interior Doors

