

Addison Township Public Library

New Building Update

Date: 9/15/2026



Construction Progress and Updates

- Egress window installation complete. (All 4 Windows)
- Hose spigots installed per concept of rear patio from SE Michigan Rural Library Grant.
- HVAC installing in progress. Ducted work on site and boring through walls needed for HVAC complete. Additional chase for duct work will be created on NE corner (shown in images).
- Plumbing installation going well (mop sink and all water lines installed.)
- Water well powered and pressurized. Will work on planning inspection from county for final approval.
- Exterior brick washing planned (week of sept. 14th).
- Exterior sealing and prep for painting in planning.
- Locksets installed for all doors. Rekeying planned for locks and keys will be provided to the library.
- Expansion joints will be added around front pillars to prevent future cracking in mortar and columns.
- Final site grading will follow immediately after the rear patio is installed.
- Low-voltage (communication wiring) can be installed at this time. TLN will be consulted and help with coordinating installation.
- Request to township has been made for release of performance agreement funds. Review with PEA (township engineer consultant) planned for 9/16/2026.

Committee Tasks

- Continuing communication with TLN to coordinate building electrical and data wiring.
 - o Requirements for IT equipment in basement has been provided to southeast commercial. Installation is being planned.
- Work with South East Commercial on interior finishes
- Review potential options for exterior signage on the building ("Addison Township Public


Library” sign) shown below.

- Committee should start talking to Southeast to understand sign lighting and any special sign requirements.
- Concepts shown below

Sign Company Rendering



Architect Rendering


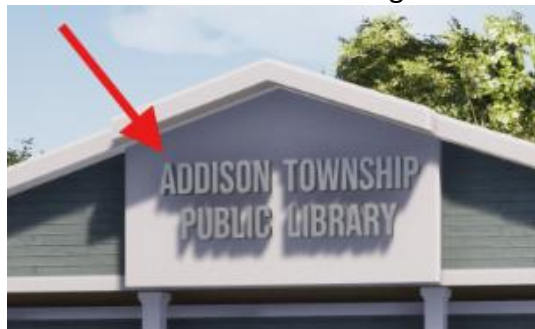


Progress Pictures

Egress Window



Hose Spigots

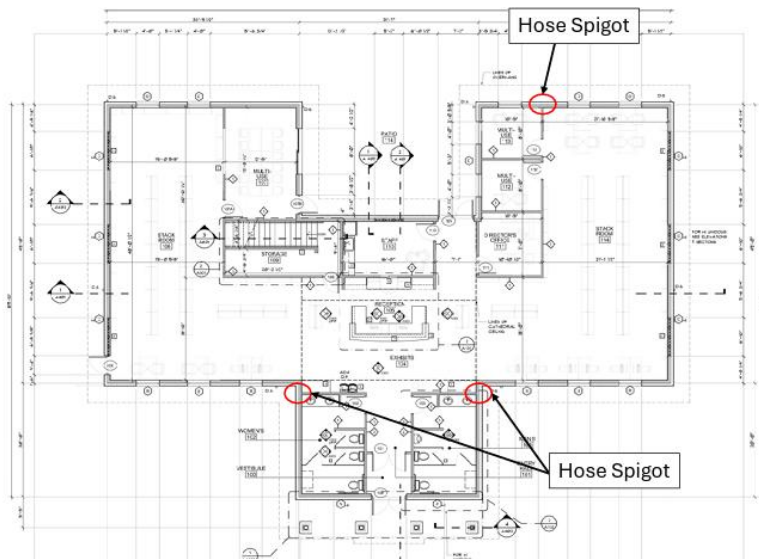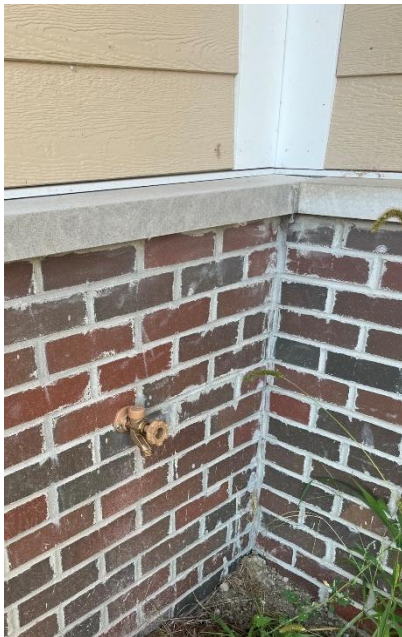

HVAC





Lockset



Plumbing

